

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	3 October 2026
Team ID	
Project Name	Automated Network Request Management System
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Network Request Catalog Item	USN-1	As an employee, I can open the Network Request catalog item in the Service Portal (/sp) and view the request form.	3	High	
Sprint-1		USN-2	As an employee, I can submit a request by entering my mobile number, type of connection, total amount, mode of payment (UPI/Card) and address.	5	High	
Sprint-1		USN-3	As an employee, I can attach supporting documents and save my request as a draft before ordering.	2	Low	
Sprint-1		USN-4	As an employee, my request is linked to my user account through the Requester Information variable set.	3	Medium	
Sprint-1	Database Table (u_database_tables)	USN-5	As an admin, I can create the custom table u_database_tables with fields for database number, mobile number, connection type, mode of payment, total amount, customer address and assignment.	5	High	
Sprint-1		USN-6	As an admin, every new record gets an auto-generated number with the DAT prefix.	2	High	

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2	Dynamic Form Validation	USN-7	As an employee, the ID field is shown only when I select Existing as the type of connection (Catalog UI Policy: visible/hide).	5	High	
Sprint-2		USN-8	As an employee, the mandatory fields change dynamically based on my connection choice (New / Existing).	5	High	
Sprint-2		USN-9	As an employee, I get immediate on-form validation for missing mandatory details (address, payment mode, amount) before I order.	3	High	
Sprint-2		USN-10	As an employee, I can choose the mode of payment (UPI or Card) on the request form.	2	Medium	
Sprint-2	Request Submission	USN-11	As an employee, I can place my order with Order Now, see the order confirmation, and receive a request number (REQ...) with a Request Summary (RITM...).	5	High	
Sprint-3	Workflow Automation (Flow Designer)	USN-12	As the system, the Network Request flow triggers from the Service Catalog and gets the catalog variables from the submitted request.	3	High	
Sprint-3		USN-13	As the system, the flow creates a record in u_database_tables (DAT...) mapped from the request variables.	5	High	
Sprint-3		USN-14	As a manager, I receive an approval request on the Database Tables record and can approve or reject it.	5	High	
Sprint-3		USN-15	As the system, the flow updates the Database Tables record according to the decision (If Approved / Else).	5	High	
Sprint-3		USN-16	As an admin, I can activate the flow and verify that it triggers on every new Network Request order.	2	Medium	
Sprint-4	Email Notifications	USN-17	As an employee, I receive an automated confirmation email with my request number after I submit a request (sys_email).	5	High	

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-4		USN-18	As an employee, the email content is dynamic and shows my name and request number in HTML format.	3	Medium	
Sprint-4	Request Tracking	USN-19	As an employee, I can track my request status, stage and estimated delivery in the Request Summary.	3	Medium	
Sprint-4		USN-20	As an IT analyst, I can view all generated records and their approval status in the Database Tables list.	3	Medium	
Sprint-4	Testing & Deployment	USN-21	As a tester, I can run an end-to-end test of order, validation, approval and email notification to confirm the system works.	3	High	
Sprint-4		USN-22	As a team, we prepare the project documentation and demo of the solution.	3	Low	

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days	07 Sep 2026	12 Sep 2026	20	12 Sep 2026
Sprint-2	20	6 Days	14 Sep 2026	19 Sep 2026	20	19 Sep 2026
Sprint-3	20	6 Days	21 Sep 2026	26 Sep 2026	20	26 Sep 2026
Sprint-4	20	6 Days	28 Sep 2026	03 Oct 2026	20	03 Oct 2026


Velocity:

The project is planned as 4 sprints of 6 days each, with a total scope of 80 story points. The velocity of the team is 20 (story points per sprint). Let's calculate the team's average velocity (AV) per iteration unit (story points per day):

$$AV = \frac{\text{velocity}}{\text{sprint duration}} = \frac{20}{6} \approx 3.33$$

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time.

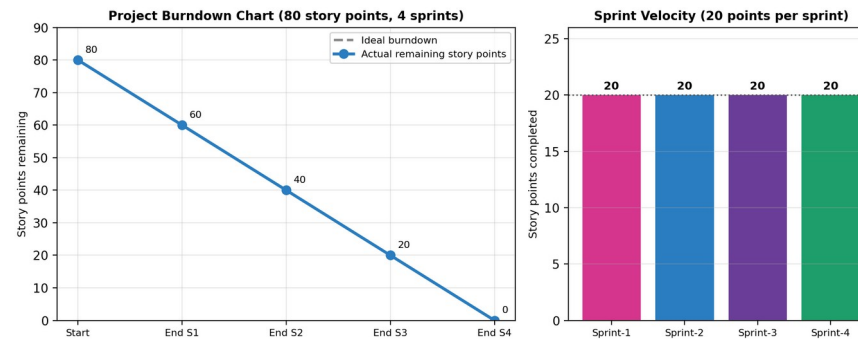

<https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>

<https://www.atlassian.com/agile/tutorials/burndown-charts>

Reference:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
